




— BUREAU OF —
RECLAMATION

Salinas and Carmel Rivers Basin Study

Study Partners Check In
February 4, 2021

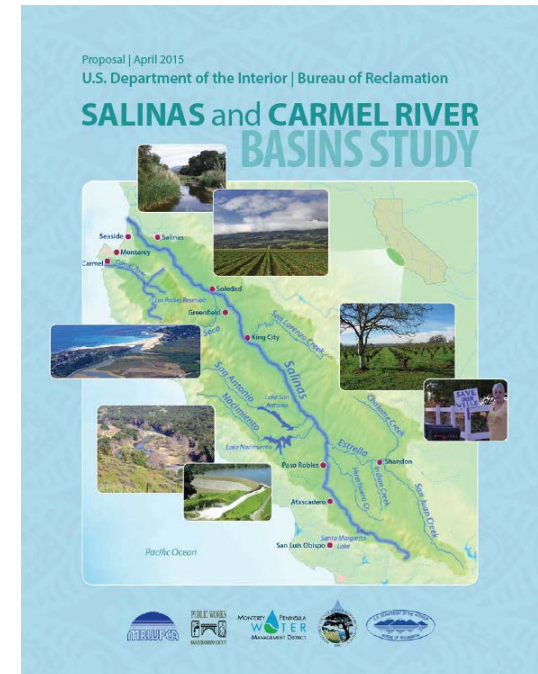

Agenda

- Management changes
- Project status
 - Brief overview
 - Explanation of project schedule delay
 - Notice regarding a February 9th briefing presentation to Monterey County Board of Supervisors – focused on TM 2 climate change scenarios approach
- Schedule update
- Next steps



Management Changes

- **Mike Dietl – USBR, Project Manager** - replacing Ankur Bhattacharya as the new Reclamation Project Manager

Contact information:


mdietl@usbr.gov

(916) 978-5070


Mid Pacific Region



Salinas and Carmel River Basin Study Approach

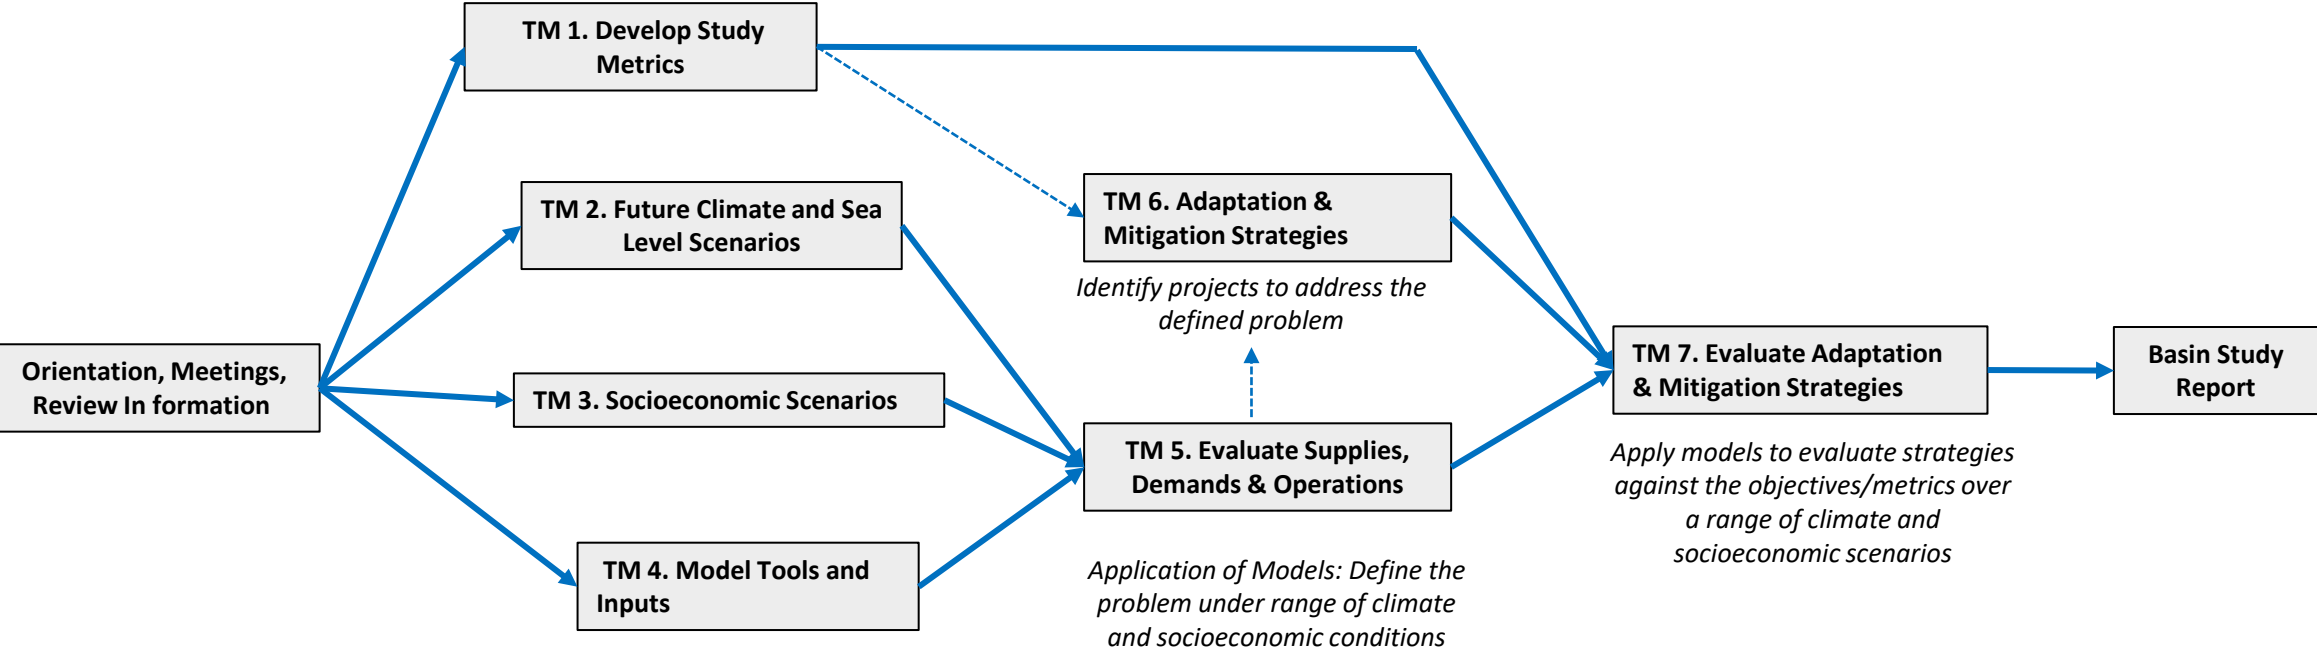

Salinas and Carmel River Basin Study Approach

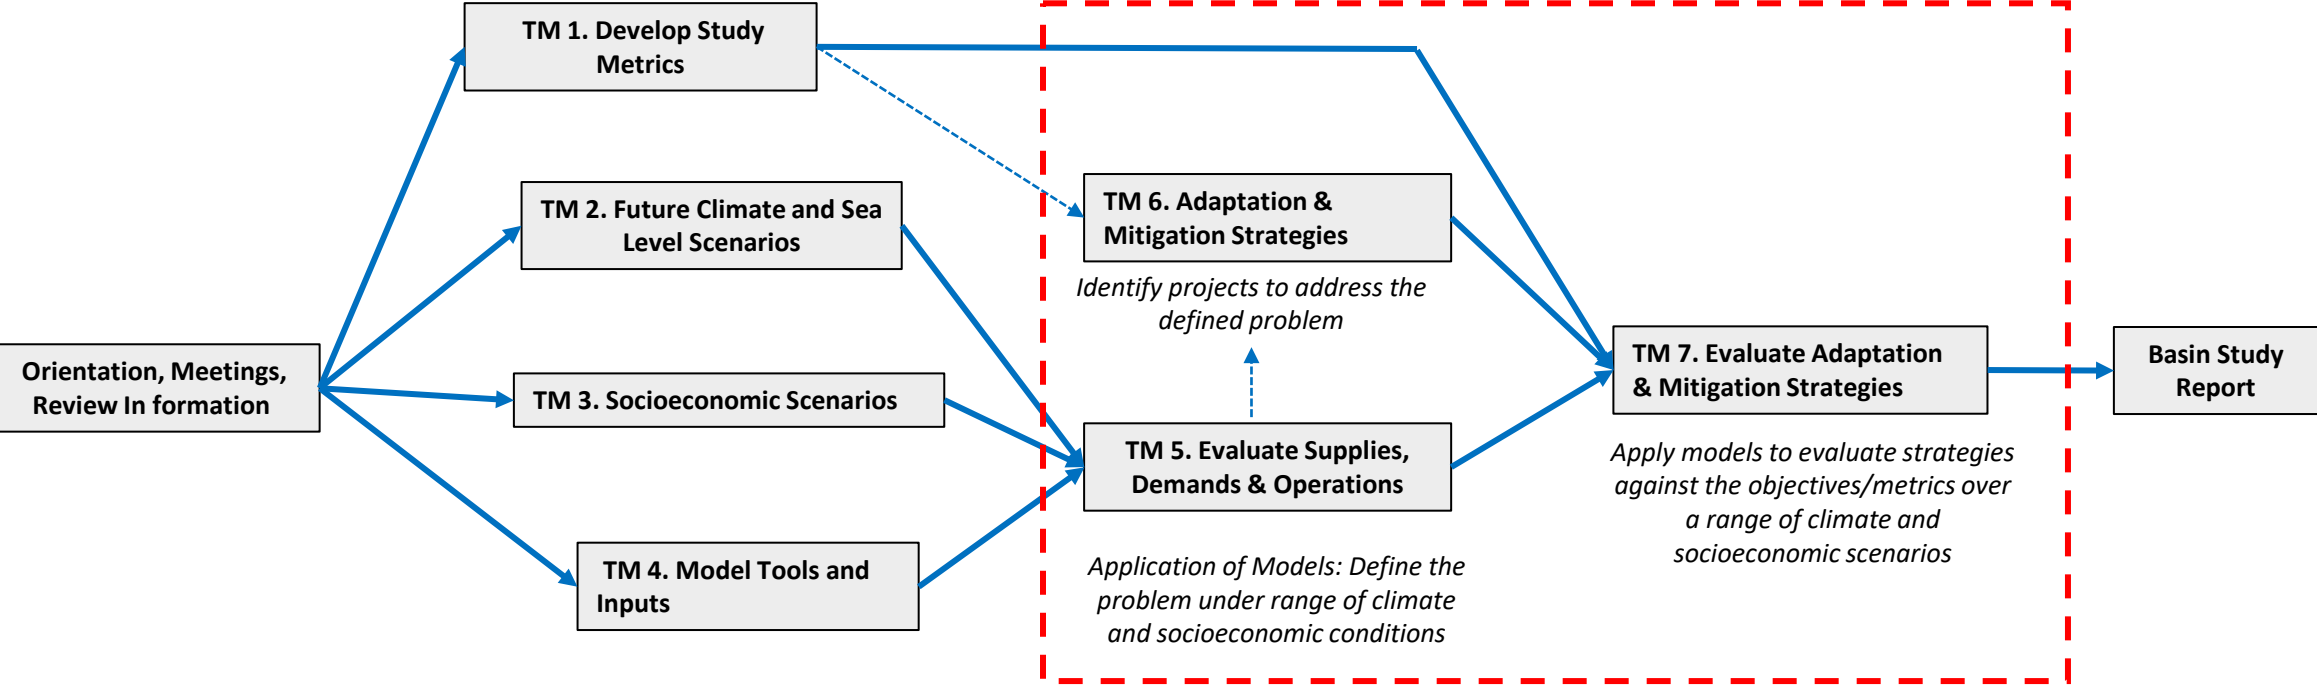

Brief Explanation of Schedule Delay




















Basin Study Progress To-Date and Schedule to Complete

- **Complete:**
 - TM 1. Study Metrics
 - TM 2. Future Climate and Sea Level Scenarios
 - TM 3. Socioeconomic Scenarios
 - TM 4. Model Tools and Inputs
- **In Progress:**
 - TM 5. Evaluate Water Supplies, Demands, and Operations
 - TM 6. Develop Adaptation and Mitigation Strategies
 - TM 7. Evaluate Adaptation and Mitigation Strategies
- **Basin Study Summary Report/Executive Summary – Late Fall 2021**



Technical Deliverable and Meeting Schedule

Task Names	Feb-21	Mar-21	Apr-21	May-21	Jun-21	Jul-21	Aug-21	Sep-21	Oct-21
Technical Documents									
Evaluate Water Supplies, Demands, and Operations - TM 5									
Develop Adaptation and Mitigation Strategies - TM 6									
Evaluate Adaptation and Mitigation Strategies - TM 7									
Prepare Basin Study Summary Report and Executive Summary									
Communications and Outreach Plan									
Partner Meetings									
Stakeholder Meetings									

-  Draft to Study Partners (P)
-  Web Presentation with Agencies
-  Document is finalized (F)
-  Key Stakeholders



Next Steps

- **Feb 9, 2021:** Briefing presentation to Monterey County Board of Supervisors
- **Late March:**
 - Receive draft TM 5 “Evaluate Water Supplies, Demands, and Operations”
 - Receive draft TM 6 “Adaptation and Mitigation Strategies”
- **Early April:** Web presentation on draft TM 5 and draft TM 6
- **Mid April:** Partner Agencies submit comments on draft TM 5 and draft TM 6
- **Early May:** Stakeholder meetings
- **Late June:** Receive draft TM 7 “Evaluate Adaptation and Mitigation Strategies”
- **Early July:** Web presentation on draft TM 7

